



# EMA tracking tool: relocation to Amsterdam

## Main milestones



**20.11.2017**

EU27 decision on Amsterdam as new EMA seat

**26.01**

Final decision on temporary building

**01.07**

Seat agreement signed by EMA and NL

**30.03**

Staff relocation to temporary building finalised

**20.01**


Staff relocation to permanent building finalised

2018

2019

2020

Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun

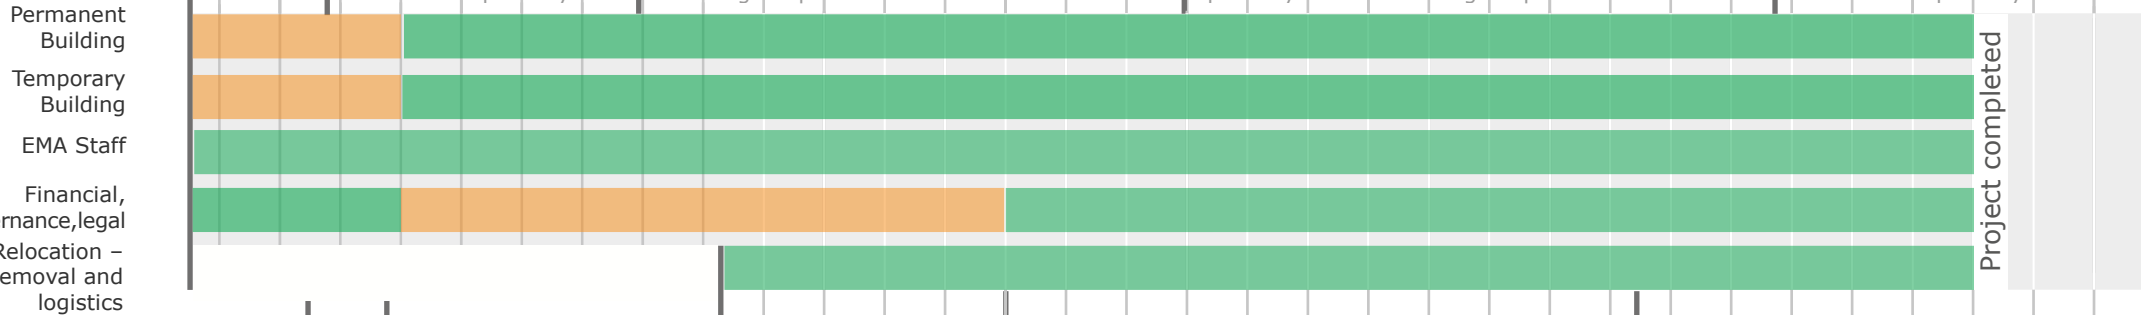

**22.02**

Approval of permanent building by Budgetary Authority as initially expected

**15.01**

Joint governance structure implemented

**09.08**

New work stream established

**01.01**


SPARK building fully operational

**15.11**

Permanent building handed over to EMA

**\*last updated on 30 April 2020**

Please click on the icons to be directed to the related work streams.  
 EMA stands for European Medicines Agency and NL stands for the Netherlands.  
 The status bar shows the current status of the work stream, including its history and, where relevant, previous changes in status.





# EMA tracking tool: relocation to Amsterdam Permanent building




**22.02**

Approval of permanent building by  
Budgetary Authority as initially expected

**15.11**

Permanent building  
handed over to EMA

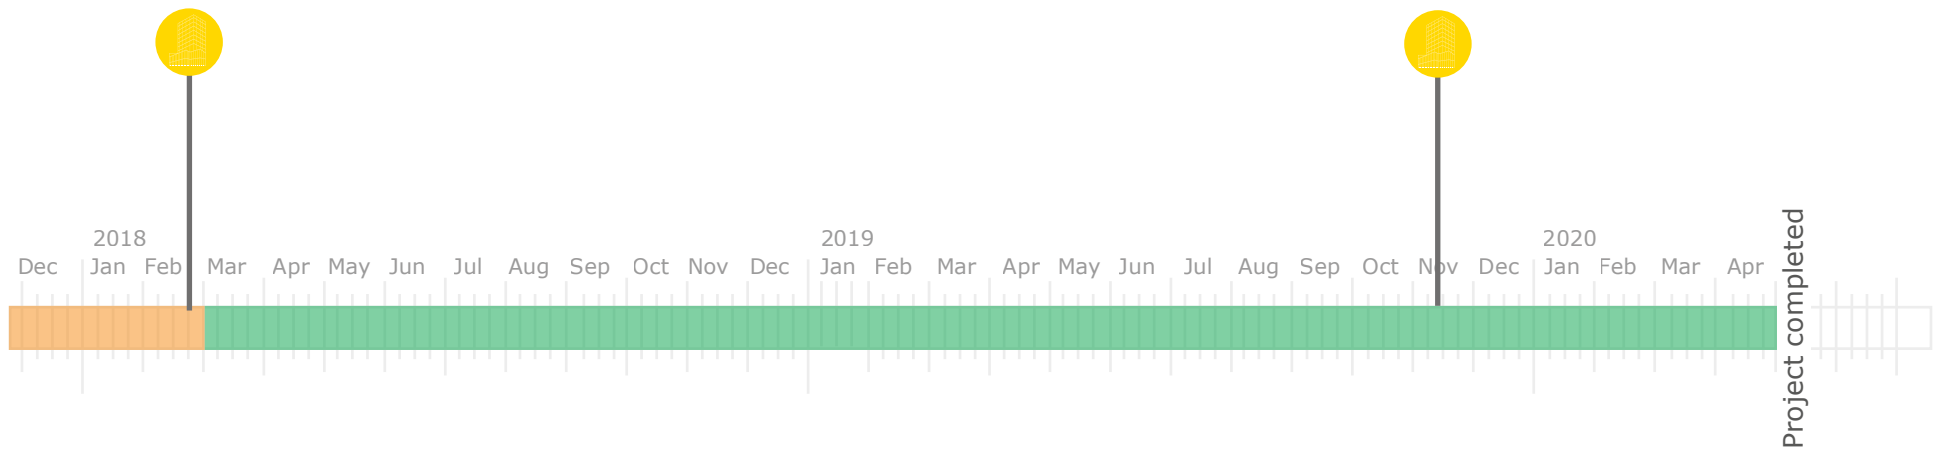

- progress on track
- progress delayed but overall still on track
- progress at risk

**\*last updated on 30 April 2020**


## Legend:

- EMA in charge
- NL in charge
- EMA+NL in charge
- EU in charge
- completed
- ongoing
- ▲ deadline missed
- not started



# EMA tracking tool: relocation to Amsterdam

## Temporary building

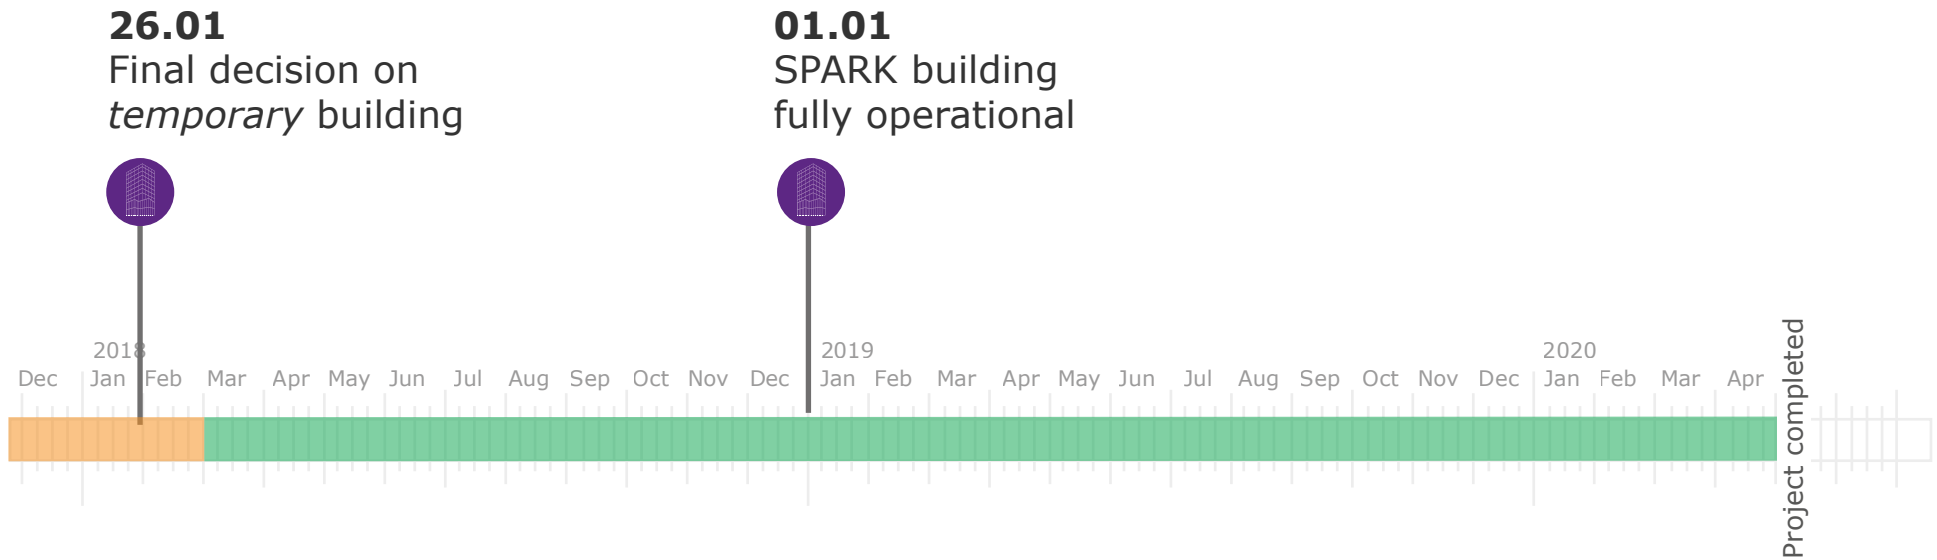

- progress on track
- progress delayed but overall still on track
- progress at risk

**\*last updated on 30 April 2020**


### Legend:

- EMA in charge
- NL in charge
- EMA+NL in charge
- EU in charge
- completed
- ongoing
- ▲ deadline missed
- not started



# EMA tracking tool: relocation to Amsterdam

## EMA Staff

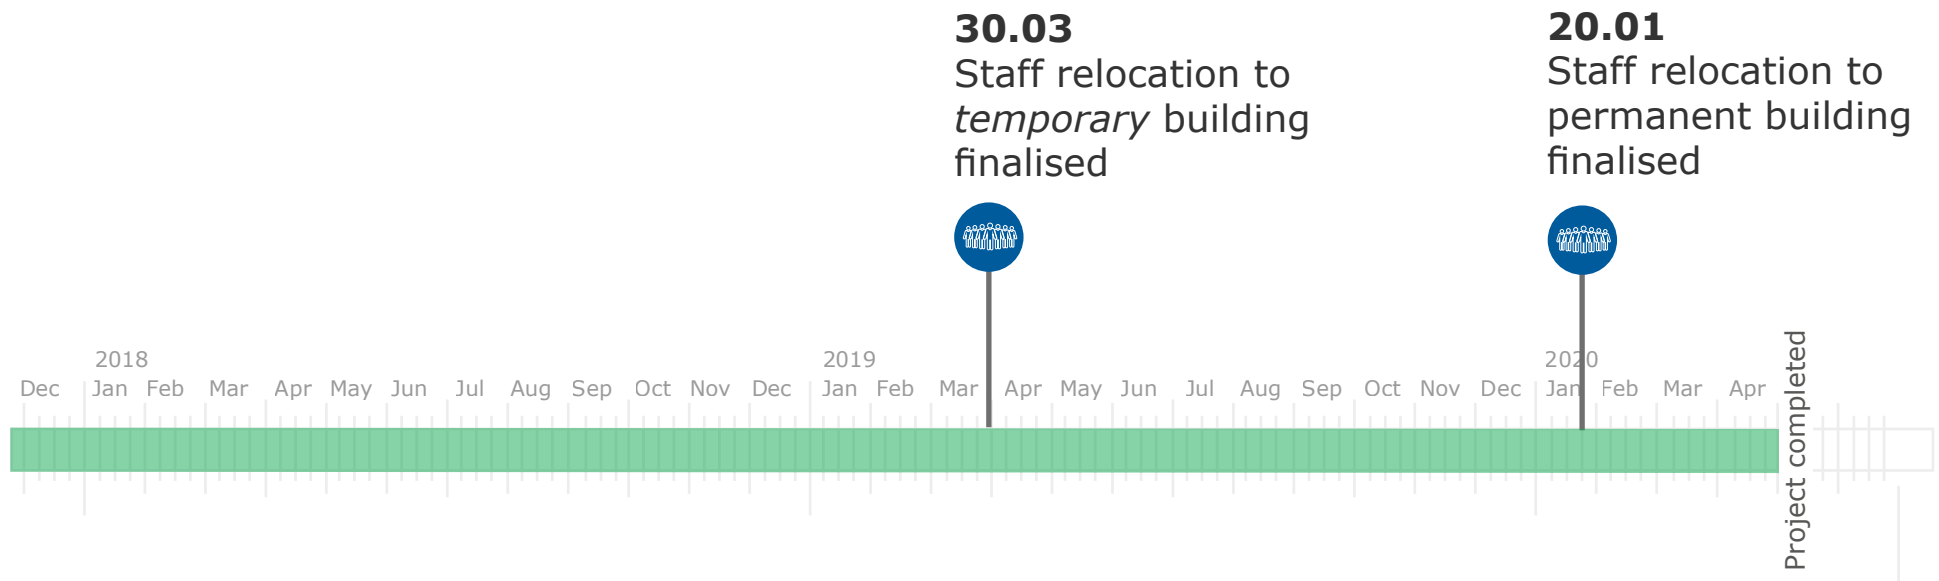

- progress on track
- progress delayed but overall still on track
- progress at risk

**\*last updated on 30 April 2020**


### Legend:

- EMA in charge
- NL in charge
- EMA+NL in charge
- EU in charge
- completed
- ongoing
- ▲ deadline missed
- not started



# EMA tracking tool: relocation to Amsterdam

## Financial, governance, legal

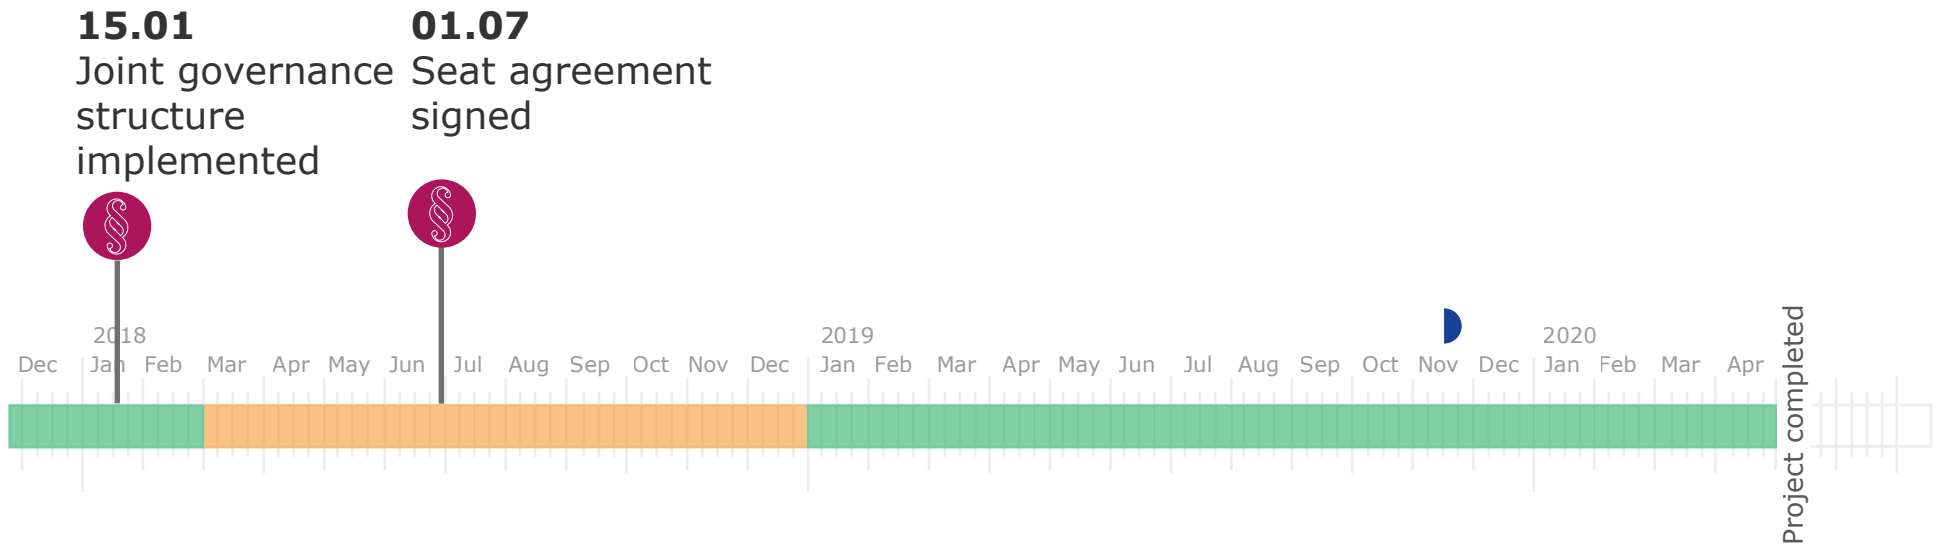

- progress on track
- progress delayed but overall still on track
- progress at risk

**\*last updated on 30 April 2020**


### Legend:

- EMA in charge
- NL in charge
- EMA+NL in charge
- EU in charge
- completed
- ongoing
- ▲ deadline missed
- not started



# EMA tracking tool: relocation to Amsterdam

## Removal and logistics

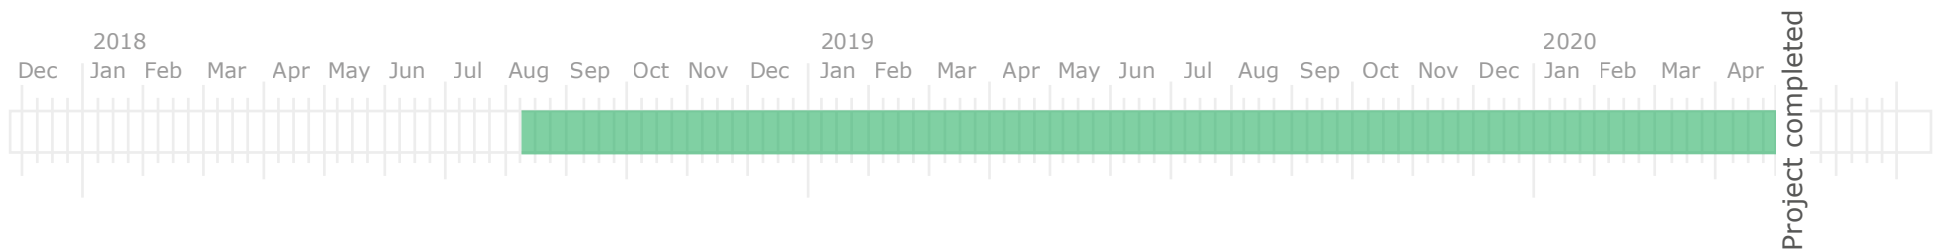

- *progress on track*
- *progress delayed but overall still on track*
- *progress at risk*

***\*last updated on 30 April 2020***

### Legend:

- EMA in charge
- NL in charge
- EMA+NL in charge
- EU in charge
- completed
- ongoing
- ▲ deadline missed
- not started
